

WORKS IN PROGRESS

1. Smart Roads Under Smart City Mission

Civil Works

- Reconstruction of Road Pavement Crust
- Storm Water Drain
- Utility Crossings Chambers
- Foot Path & Landscape Works
- Road Furniture


Services

- Water Supply Lines
- Sewage Lines
- Electrical
- OFC
- Gas Lines

Estimate Cost : Rs 123,58,78,380.00/- (Excl. GST)

Stipulated date of completion 23-09-2023.

Status: 15% of the work is completed

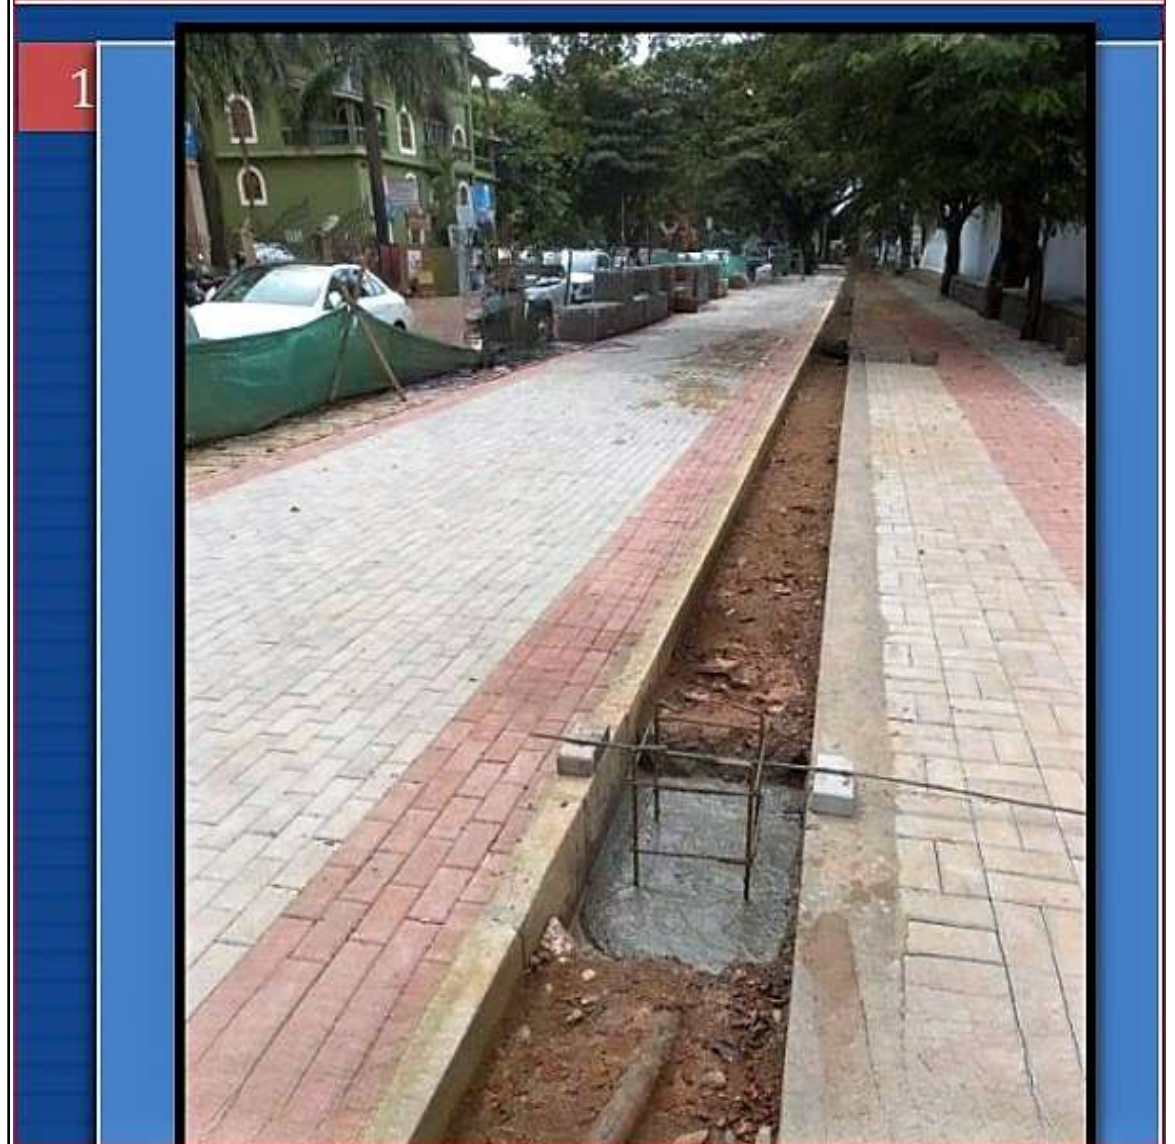

Mormugao Council

2. Mormugao Fish Market

Renovation and repair of Mormugao Municipal Council Building at Vasco Goa (Deposit Work).

Estimate Cost: Rs. 8.84 cr.

Stipulated date of completion 03-09-2023.

Status: Dismantling of existing structure in progress



Mormugao Council

3. Mormugao Council Building

Renovation and repair of Mormugao Municipal Council Building at Vasco Goa (Deposit Work).

Estimate Cost: Rs. 8.84 cr.

Stipulated date of completion 03-09-2022.

Extended date of completion 31-12-2022

Status: 60% of work is completed



Mapusa Council

4. Saraswat Vidyalaya - Khorlim Mapusa

Development of playground of Saraswat Vidyalaya, Khorlim, Mhapsa Goa under FRANCIS Urban Connect Scheme 2013.

Estimate Cost: Rs. 1,90,94,804.

Stipulated date of completion 31-03-2023.

Status: 40% work is completed



Mapusa Council

5. Mapusa Garage

Development of Mapusa Garage on plot bearing Chalta No. 67 of P. T. Sheet no. 135 & Chalta no. 7 & 12 of P.T. Sheet No. 147 for Mhapsa Municipal Council (Commercial Complex with Basement, Ground + 6 floors).

Estimate Cost: Rs. 17,38,24,409.

Stipulated date of completion 31.3.2023.

Status: 50% work is completed



Valpoi Council

6. Valpoi Municipal Council

Proposed Development of open space in Sy. No. 19/1 as Safe Play Area at Valpoi Sattari under Francis Urban Connect Scheme, 2013.

Estimate Cost: Rs. 0.93 cr.

Stipulated date of completion 31.10.2022.

Status: Completed and is in the handing over stage



Pernem Council

7. Pernem Municipal Council

Construction of New Administrative building - survey no. 501/1 and 501/3 at Pernem Municipal Council

Estimate Cost: Rs. 8,72,23,357/-

Stipulated date of completion 20-Aug-2023

Status: 25% of the work is completed.



Canacona Council

8. Canacona Municipal Council

Reconstruction and extension of Municipal Building in Sy. No. 52/2 for Canacona Council.

Estimate Cost: Rs. 7.87 cr.

Stipulated date of completion 26.03.2023.

Status: Footing work in progress

